The Business Pain Point Driving This Project

Sarvdev Technology (est. 2022), a manufacturer of PVC plates/holders and electric boards, lost easy retailer access after relocating from Mayur Vihar to Shahdara. Retailers expect dealer/supplier-arranged delivery, forcing reliance on costly on-demand couriers (mainly Porter) and inconsistent self-delivery — driving up transport cost and weakening distribution reliability.

IN SCOPE

- Mapping retailer clusters & order volumes across Delhi-NCR
- Identifying & onboarding local/hyperlocal delivery partners
- Pilot with 1-2 partners on high-order routes
- Cost-and-performance scorecard vs the Porter baseline

OUT OF SCOPE

- Owning or operating a company delivery fleet
- Building an in-house logistics/technology platform

THE 6 KEY DELIVERABLES REQUIRED

1. Retailer & order-volume mapping report
2. Shortlist of verified local delivery partners
3. Partner profiles with capability summary
4. Signed onboarding agreements / rate cards
5. Pilot rollout plan (1-2 partners, priority routes)
6. Cost-and-performance scorecard (time, cost/drop, satisfaction)

Retailer & Order-Volume Mapping + Verified Local Partner Shortlist

DELIVERABLE 1

Retailer & Order-Volume Mapping Report

Problem: No documented view of retailer location or order density existed to plan delivery routes.

Method: Geo-tagged 30 retailers into 10 clusters / 6 route groups; ranked by a Pareto (cumulative share) calculation.

Cluster	Route	Avg Daily Orders	Priority
Shahdara	R1	102	P1 - High
Seelampur	R1	84	P1 - High
Welcome + Laxmi Nagar	R2	138 (combined)	P2 - Medium
Preet Vihar + Mayur Vihar	R3	114 (combined)	P2 - Medium

186
orders/day — Shahdara + Seelampur (Route R1), the top-priority pilot cluster

30 / 10
retailers mapped across 10 clusters, 3 zones

Result & Evidence: Complete ranked mapping report; R1 objectively confirmed top pilot priority. Signed off 19-Aug-2026 — see 'D1 Retailer Mapping'.

DELIVERABLE 2

Shortlist of Verified Local Delivery Partners

Problem: No objective basis existed to compare informal local riders against established platforms.

Method: 5-criterion weighted scoring model (Coverage 25%, Cost 25%, Vehicle Fit 15%, Tracking 15%, Scalability 20%) applied to 8 candidates.

Partner	Category	Weighted Score	Decision
Kusum Delivery	Local	3.50	**SHORTLISTED (R2)**
Uncle Delivery	Local	3.35	**SHORTLISTED (R1)**
Umaa Delivery	Local	3.20	**RESERVED (scale-up)**
Shadowfax	Established	4.35	Verified

8
candidate partners scored (3 local + 5 established)

2
local partners shortlisted for the pilot (Uncle + Kusum)

Result & Evidence: Kusum Delivery and Uncle Delivery shortlisted for the pilot; Umaa Delivery reserved for scale-up. Signed off 21-Aug-2026 — see 'D2 Partner Shortlist'.

Partner Capability Profiles + Signed Onboarding Agreements

DELIVERABLE 3

Partner Profiles with Capability Summary

Problem: A score alone is not enough detail to brief management or negotiate terms.

Method: Field interviews for 3 local partners; official-website verification for 5 established companies.

Partner	Coverage	Vehicle	Best Fit
Uncle Delivery	Shahdara belt	2W	R1, R2
Kusum Delivery	E. Delhi + Noida border	2W + 3W	R2, R3
Umaa Delivery	E. Delhi, Ghaziabad, Noida	3W / Tempo	R4

Tracking / POD across all 3 local partners: phone/WhatsApp confirmation or manual delivery register — no app tracking yet (field-verified, RFQ pending).

8
complete capability profiles produced (local + established)

5
official sources verified (Shadowfax, Porter, Borzo, LoadShare, Zypp)

Result & Evidence: Decision-ready profiles for all 8 candidates. Signed off 27-Aug-2026 — see 'D3 Partner Profiles'.

DELIVERABLE 4

Signed Onboarding Agreements / Rate Cards

Problem: A shortlist is not a commercial commitment — nothing bound partners to a rate or SLA.

Method: Due diligence and rate negotiation, then signed agreements with rate card, SLA and payment terms.

Partner	Route	Signed Rate	SLA	Status
Uncle Delivery	R1	₹58/drop	≤3.0 h	SIGNED
Kusum Delivery	R2	₹68/drop	≤3.5 h	SIGNED
Umaa Delivery	R3/R4	₹80/drop (indic.)	≤4.5 h	PENDING

Porter baseline used for comparison: ₹90-120/drop (₹105 mid-point). Both signed rates are well below baseline.

2
binding onboarding agreements signed (Uncle + Kusum)

₹30.5k
projected monthly saving on R1+R2+R3+R4 vs Porter baseline

Result & Evidence: 2 signed agreements with fixed rates below baseline; Umaa held in reserve. Signed off 03-Sep-2026 — see 'D4 Onboarding Agreements'.

Pilot Rollout Plan + Cost-and-Performance Scorecard

DELIVERABLE 5

Pilot Rollout Plan (1-2 Partners, Priority Routes)

Problem: Signed rates do not prove real-world performance without a controlled test.

Method: A 4-day rollout (1 orientation + 3 live-tracking days) on Routes R1/R2 with Uncle Delivery and Kusum Delivery.

Day 0	Day 1-2	Day 3	Day 4
04 Sep	07-08 Sep	09 Sep	10 Sep
Rollout orientation	Live pilot run + tracking	Final day + satisfaction survey	Consolidate scorecard

Success criteria (agreed with management): Cost/drop ≤ ₹70; delivery time 2-4h; on-time ≥ 90%; satisfaction ≥ 4/5.

324
avg. daily orders in pilot scope (R1+R2, priority retailers)


5/5
planned rollout stages completed on schedule

Result & Evidence: Pilot executed exactly as planned, 07-09-Sep-2026. Signed off 04-Sep-2026 — see 'D5 Pilot Rollout Plan'.

DELIVERABLE 6

Cost-and-Performance Scorecard

Method: 3-day pilot log (cost, time, on-time, satisfaction) compared against the Porter baseline and agreed targets.

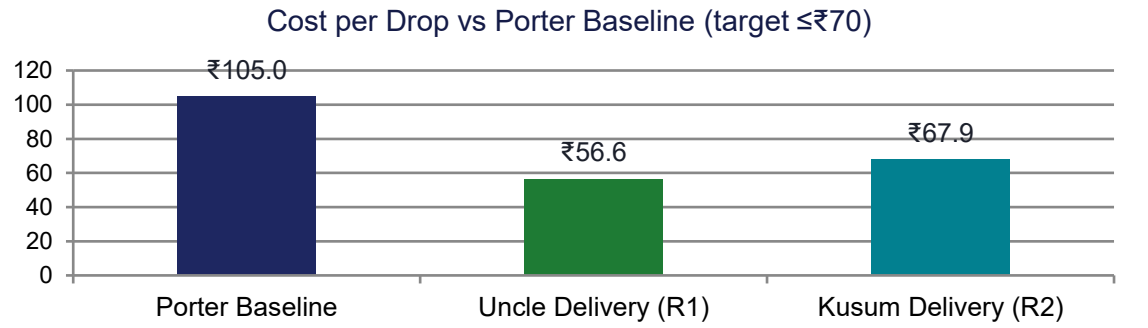

Metric	Target	Uncle (R1)	Kusum (R2)
Delivery time	2-4 h	2.6 h ✓	3.1 h ✓
On-time rate	≥ 90%	87.7%	87.6%
Satisfaction	≥ 4/5	4.03 ✓	3.93

Result & Evidence: Both partners beat Porter on cost/drop and delivery time. On-time % and satisfaction trending up but below target after 3 days — flagged honestly; recommend 2-week extended monitoring before scale-up. Signed off 10-Sep-2026 — see 'D6 Pilot Log & Scorecard'.

Evidence: How Each Problem Was Solved & Results Achieved

6 / 6
key deliverables completed & signed off

21
working days used (vs 27-day baseline)

₹30.5k
projected monthly saving (R1+R2+R3+R4 vs Porter)

–46%
avg. cost/drop reduction vs Porter baseline

Deliverable	Result Achieved	Evidence (Excel Sheet)	Date
1. Retailer & order-volume mapping	R1 (Shahdara+Seelampur, 186 ord/day) confirmed top priority via Pareto ranking of 30 retailers/10 clusters	D1 Retailer Mapping	19-Aug
2. Verified local partner shortlist	Kusum (3.50) & Uncle (3.35) shortlisted from 8 scored candidates via weighted model	D2 Partner Shortlist	21-Aug
3. Partner capability profiles	8 decision-ready profiles (coverage, fleet, tracking, open questions) completed	D3 Partner Profiles	27-Aug
4. Signed onboarding agreements	2 signed agreements at ₹58/₹68 per drop, well below ₹90-120 Porter baseline	D4 Onboarding Agreements	03-Sep
5. Pilot rollout plan	4-stage rollout on R1/R2 executed exactly as planned, 07-09-Sep	D5 Pilot Rollout Plan	04-Sep
6. Cost-and-performance scorecard	Cost/drop & time beat Porter; on-time% & satisfaction trending up, monitored honestly	D6 Pilot Log & Scorecard	10-Sep

Overall management recommendation: Adopt Uncle Delivery and Kusum Delivery as the primary carriers for Routes R1/R2, replacing the Porter on-demand baseline, subject to a 2-week extended monitoring period to confirm the on-time and satisfaction trend clears the 90% / 4-of-5 thresholds before scaling to R3/R4 with Umaa Delivery.

Work Completed: 11-Aug-2026 to 11-Sep-2026 (24 Working Days)

Phase 0
Kickoff
11 Aug
Charter sign-off
✓ COMPLETED

→

Phase 1
Retailer & Route Mapping
12-19 Aug
Deliverable 1
✓ COMPLETED

→

Phase 2
Partner Shortlist & Profiling
20-27 Aug
Deliverables 2, 3
✓ COMPLETED

→

Phase 3
Onboarding & Rate Cards
28 Aug-03 Sep
Deliverable 4
✓ COMPLETED

→

Phase 4
Pilot Rollout & Execution
04-09 Sep
Deliverable 5
✓ COMPLETED

→

Phase 5
Scorecard & Final Submission
10-11 Sep
Deliverable 6
✓ COMPLETED

Schedule compression: The original M3/M4 charter baseline planned 27 working days (11-Aug to 18-Sep-2026) across two 27-day critical paths (CP-1, CP-2). By running due-diligence/rate-negotiation in parallel with partner profiling, and compressing pilot planning into pilot execution, the team completed all 6 deliverables 3 working days early — within 24 working days.

21	27	6 days	100%
working days used	original baseline (working days)	ahead of schedule	of deliverables completed

Final outcome: All 6 faculty-required deliverables were completed, signed off and evidenced inside the 11-Aug to 11-Sep-2026 window, with a working pilot on Sarvdev's two highest-priority retailer routes and a documented, honest cost-and-performance scorecard ready for management decision-making.
